ADB

12 March 2026

H.E. Im Sethyra
Royal Government Delegate in charge as
Director General
Ministry of Economy and Finance
Royal Government of Cambodia

Your Excellency:

Subject: **Loan 3684-CAM and Grant 0591-CAM: Second Urban Environmental Management in the Tonle Sap Basin Project—No objection to the Social Safeguards Monitoring Report on Land Acquisition and Involuntary Resettlement**

We refer to Your Excellency's letter dated 3 March 2026 requesting ADB's no objection to the Social Safeguards Monitoring Report on Land Acquisition and Involuntary Resettlement for the subject project, covering the period from October to December 2025.

The report provides detailed and sufficient information on the implementation of the detailed resettlement plan for the four realigned drainage networks of the wastewater treatment plant subproject in Serei Saophoan. Accordingly, we have no objection to the report. It was disclosed on the project website on 6 March 2026 at the following link https://www.adb.org/projects/documents/cam-50102-002-smr-14.

Mr. Ratha Sann can be contacted at rsann@adb.org, should additional information be required.

Please accept, Your Excellency, the assurance of our highest consideration.

Yours sincerely,

Siti Hasanah
Unit Head, Project Administration
Water and Urban Development Sector Office
Sectors Department 2

ASIAN DEVELOPMENT BANK
6 ADB Avenue, Mandaluyong City
1550 Metro Manila, Philippines
Tel +63 2 8632 4444
Fax +63 2 8636 2444
www.adb.org

cc: H.E. Ros Seilava, Secretary of State, MEF
H.E. Pen Thirong, Secretary of State, MEF
H.E. Ms. Koy Sodany, Permanent Secretary of State, MPWT
H.E. Vong Pisith, Under Secretary of State, Project Director, MPWT
H.E. Chhuon Samrith, Under Secretary of State, MEF
H.E. Houl Bonnaroth, Director General, GDICDM, MEF
Mr. Meas Sam An, Deputy Director General, GDICDM, MEF
Mr. Chann Thorn, Deputy Director General, GDR, MEF
Mr. Kim Sothearith, Director, DMC, GDICDM, MEF
Mr. Non Wattanak, Director, DPPM, GDICDM, MEF
Mr. Kim Chanvibol, Director, RD3, GDR, MEF
Mr. Kong Ratha, Director, DIMDM, GDR, MEF
Ms. Veng Youim, Deputy Director, DMC, GDICDM, MEF
Mr. Chan Sopanhavorn, Deputy Director, DMC, GDICDM, MEF
Mr. Chum Kiry, Deputy Director, DIMDM, GDR, MEF
Ms. Ieng Sreyleap, Chief, OMC1, DMC, GDICDM, MEF

Ministry of Economy and Finance

General Department of Resettlement

Social Safeguards Monitoring Report

CAM: Second Urban Environmental Management in the Tonle Sap Basin Project

The Change in Alignment of the Four Sewerage Lines under the Wastewater and Drainage Subproject (Serei Saophoan)

Monitoring Period: October 2025 to December 2025

Prepared by the General Department of Resettlement (GDR) of the Ministry of Economy and Finance, Cambodia, for the Asian Development Bank (ADB).

TABLE OF CONTENTS

ABBREVIATIONS **3**

1. INTRODUCTION **4**

1.1 BACKGROUND OF THE PROJECT 4

1.2 BACKGROUND OF THE SUBPROJECT 4

1.3 PURPOSE OF THE REPORT 5

2. INSTITUTIONAL ARRANGEMENTS **5**

3. SCOPE OF LAND ACQUISITION AND RESETTLEMENT **6**

4. PROGRESS OF CONTRACT SIGNING AND COMPENSATION PAYMENT **7**

5. LIVELIHOOD RESTORATION PROGRAM **8**

6. DEVELOPMENT OF RESETTLEMENT SITE AND RELOCATION **8**

7. IMPLEMENTATION SCHEDULE **8**

8. GRIEVANCE REDRESS MECHANISM **9**

9. PUBLIC CONSULTATION MEETINGS **9**

10. CONCLUSION AND RECOMMENDATION **9**

List of Table:

Table 1: Summary of the Project and the Subproject Data and Milestone Dates 5
Table 2: Institutional Roles and Responsibilities of the GDR 6
Table 3: Summary of LAR Impacts by Type under the Change in Alignment 7
Table 4: Summary of Information on Actual Budget Expenditure against the Estimated Budget 8
Table 5: Actual and Tentative Implementation Schedule of Resettlement Activities 8

List of Figure:

Figure 1: The Change in alignment Sewerage Lines on PR56A, NR5, and BMC Road 4

List of Annexes:

Annex A: Contract Signing Stage 10
Annex B: Compensation Stage 14

CK

ABBREVIATIONS

ADB	-	Asian Development Bank
AHs/APs	-	Affected Households/Persons
DIMDM	-	Department of Internal Monitoring and Data Management
DRP	-	Detailed Resettlement Plan
EA	-	Executing Agency
GDR	-	General Department of Resettlement
GRM	-	Grievance Redress Mechanism
IRC	-	Inter-Ministerial Resettlement Committee
IRC-WG	-	Inter-Ministerial Resettlement Committee Working Group
IRP	-	Income Restoration Program
LAR	-	Land Acquisition and Involuntary Resettlement
MEF	-	Ministry of Economy and Finance
MPWT	-	Ministry of Public Works and Transport
NR	-	National Road
PMU	-	Project Management Unit
PGRC	-	Provincial Grievance Redress Committee
PR	-	Provincial Road
RGC	-	Royal Government of Cambodia
ROW	-	Right-of-Way
SMR	-	Social Safeguards Monitoring Report
SOP	-	Standard Operating Procedures for Externally Financed Projects in Cambodia
USD	-	United States Dollar

1. INTRODUCTION

1.1 BACKGROUND OF THE PROJECT

1. The Second Urban Environmental Management in the Tonle Sap Basin (TS2), or the Project) funded by the Asian Development Bank (ADB) will improve the urban environmental services in Battambang, Serei Saophoan and Stung Saen, three of Cambodia's provincial cities located around the Tonle Sap Lake. The Project will also improve institutional effectiveness to provide sustainable services and support an improved policy and planning environment for wastewater and solid waste management.

2. The Project is classified as Category "B" for Involuntary Resettlement (IR) impacts. The loan and grants were approved on 01 August 2018 and became effective on 14 December 2018. The original closing date of the loan and grants was on 27 June 2024. However, the closing date was extended to 30 June 2026.

1.2 BACKGROUND OF THE SUBPROJECT

3. The Subproject comprises of the Wastewater and Drainage and Solid Waste Management Subproject in Serei Saophoan. The Detailed Resettlement Plan (DRP) for the Subproject was approved in March 2021. A Resettlement Report on additional scope on Drainage Line B was prepared and approved in April 2024. The implementation of the DRP and the Resettlement Report is fully completed. During the monitoring period, there was a change in alignment of Four Sewerage Lines on PR56A, BMC Bank Road and NR5 (2 Lines). Figure 1 shows the change in alignment of sewerage lines on PR56A, NR5, and BMC Road.

Figure 1: The Change in alignment Sewerage Lines on PR56A, NR5, and BMC Road

4. A DRP for the was prepared for the additional scope of works because of the new change in alignment of the four sewerage lines and was approved by the Inter-Ministerial Resettlement Committee (IRC) on 26 September 2025 and subsequently endorsed by the ADB on 9 October 2025. The cut-off date for eligibility for the new impacts because of the changes in the alignment was established on 07 May 2025. Table 1 summarizes the data and milestone dates for the Project and the change in alignment.

Table 1: Summary of the Project and the Subproject Data and Milestone Dates

Project Name	**Second Urban Environmental Management in the Tonle Sap Basin Project**
Loan/Grant/Credit Number	ADB Loan 3684-CAM, and ADB Grant 0591-CAM
Date of Approval of Loan and Grant	01 August 2018
Name of Subproject	The Wastewater and Drainage and Solid Waste Management Subprojects
Name of Additional Scope of IR Impacts	The Change in Alignment of Four Sewerage Lines on PR56A, BMC Bank Road and NR5 (2 lines)
Name of Province	Serei Saophoan, Banteay Meanchey Province
Detailed Design and Demarcation of Land Completed	06 May 2025
Cut Off Date for Eligibility	07 May 2025
DRP Approved by IRC	26 September 2025
DRP Endorsed by ADB	9 October 2025

1.3 PURPOSE OF THE REPORT

5. The original DRP and the Resettlement Report for the first set of additional scope have been fully implemented and progress in their implementation was reported in the previous Semi-Annual Monitoring Report (SMR). This SMR covers the reporting on the DRP for the additional scope of works because of the change in alignment of the four sewerage lines which was endorsed by the ADB on 9 October 2025. The purpose is to measure and report on the progress in the implementation of the new DRP, identify problems and risks, if any, and measures to mitigate them as well as assess if the compensation and rehabilitation assistance are paid in accordance with the provisions under the DRP approved and covers the monitoring period from October 2025 to December 2025.

2. INSTITUTIONAL ARRANGEMENTS

6. There is no change in the institutional arrangements for the implementation, monitoring and reporting of the DRP The Project is implemented by the Ministry of Public Works and Transport (MPWT) as the Executing Agency (EA) through the Project Management Unit (PMU) which supports the MPWT in undertaking overall oversight and management of the Project. The responsibility for the preparation of the DRP, its implementation, monitoring and reporting are undertaken by the GDR in accordance with its mandate.

7. The GDR, as the permanent secretariat of the IRC, is the lead agency directly responsible for the preparation, implementation, monitoring and reporting of the LAR activities under the DRP. The

Resettlement Department 3 (RD3) of the GDR has been assigned to undertake the LAR activities under the Project.

8. The DIMDM of the GDR is responsible for carrying out the internal monitoring and reporting of the implementation of the DRP. Table 2 illustrates the institutional roles and responsibilities of the GDR for undertaking Involuntary Resettlement Safeguards.

Table 2: Institutional Roles and Responsibilities of the GDR

Activities	Responsible Agencies
Finalization of sites/alignments/land boundaries for subproject	EA/PMU, PIU
Consultation with communities and APs during project preparation	PMU/ADB/Project Preparation Consultants/ Provincial PIU/GDR
Conducting Census of all APs	GDR, PMU and EA
Conducting DMS	GDR/PRSC-WG
Preparation of draft DRP	GDR/RD3
Preparation of RCS and calculation of replacement cost units	RCS Consultant recruited by GDR
Consultation meetings with all APs and other stakeholders	GDR, IRC-WG and PRSC-WG and local authorities
Endorsement and approval of the DRP	IRC and ADB
Approval of budget for DRP implementation	RGC/MEF
Preparation of Compensation Packages and Contracts	GDR/RD3/DIMDM
Payment of Compensation	GDR, IRC/WG and PRSC/PRSC-WG
Grievance Redress Mechanism	Local District Administration /GDR/PGRC
Internal Monitoring and Reporting on Implementation of DRP	DIMDM/GDR
Semi-annual Social Safeguards Monitoring Report on the Implementation of the DRP (to ADB)	DIMDM/GDR

3. SCOPE OF LAND ACQUISITION AND RESETTLEMENT

9. The change in alignment of the four sewerage lines has brought resettlement impacts as outlined in categories below:

3.1. Impact on AHs

10. A total of 74 AHs who are business owners/259 APs were impacted. No AH was physically displaced, 74 AHs were economically displaced as they encounter partial or marginal economic impacts, and no AH is physically and economically displaced.

3.2. Impact on Land Type

11. There was no impact on privately owned land as all works were undertaken on unencumbered public land within the right-of-way (ROW).

3.3. Impact on Structures

12. There was no impact on primary structures (Houses). However, there were impacts on secondary structures comprising brick fences, sign boards and extended eaves of 670.24m2 of 65 AHs and 2.00m of concrete posts of 1 AH.

3.4. Impact on Crops and Trees

13. No crops were affected. However, a total of 22 trees of 20 AHs on state-owned land were affected. These included 16 fruit trees of 15 AHs and 6 non-fruit trees of 5 AHs.

3.5. Other Impacts

14. No AHs experienced any major impacts, permanent loss of livelihood, relocation to another site and there were no vulnerable AHs.

15. The IR impacts are summarized in Table 3.

Table 3: Summary of LAR Impacts by Type under the Change in Alignment

No.	Impact Type	Quantity (measurement units)
1	Affected Households/Affected Persons	74 AHs/259 APs
2	Physically Displaced	None
3	Economically Displaced	74 AHs
4	Physically and Economically Displaced	None
5	Primary Structures (commercial)	None
6	Secondary Structures (commercial)	670.24m2 of 65 AHs, 2.00m of 1 AH
7	Fruit Tress (various)	16 of 15 AHs
8	Non-fruit Trees (various)	6 of 5 AHs
9	Major Impact	None
10	Permanent Loss of Livelihood	None
11	Relocation to another site	None
12	Vulnerable AHs	None

Source: DRP for the change in alignment of the four sewerage lines

4. PROGRESS OF CONTRACT SIGNING AND COMPENSATION PAYMENT

16. The contract signing was conducted and concluded in October 2025. The contracts for the compensation packages have been signed by all AHs, achieving a completion rate of 100%.

17. Following this, compensation payments to all 74 AHs were successfully and fully disbursed on 24 October 2025. The total compensation payments amounted to 20,261.77 USD which is same as

the budget estimated in the DRP. Table 4 shows the details of actual expenditures against the estimated budgets specified in the DRP.

18. The full list of compensation recipients was validated against the eligibility criteria during both contract signing and payment processes. As a result, all entitled 74 AHs met the required eligibility, and no ineligible recipients were included or any eligible AH mistakenly omitted. Furthermore, it was verified that the affected assets, including secondary structures, fruit trees, and non-fruit trees, were accurately identified, and compensation payments were made as appropriate.

Table 4: Summary of Information on Actual Budget Expenditure against the Estimated Budget

Entitlement Category	Estimated Budget in DRP ($)	Variance ($)	Actual Expenditure ($)	Percentage Disbursed (%)
Secondary Structures	19,309.77	-	19,309.77	100%
Fruit Trees	697.00	-	697.00	100%
Non-Fruit Trees	255.00	-	255.00	100%
Total	**20,261.77**	-	**20,261.77**	100%

5. LIVELIHOOD RESTORATION PROGRAM

19. There were no AHs who lost any source of their livelihoods permanently and hence there was no Livelihood Restoration Program under the DRP.

6. DEVELOPMENT OF RESETTLEMENT SITE AND RELOCATION

20. Since there was no physical displacement of any AH to a new site, there was no requirement for providing a resettlement site under the DRP.

7. IMPLEMENTATION SCHEDULE

21. All compensation payments were completed on 24 October 2025. The sites with all cleared encumbrances were handed over to the MPWT in 17 November 2025. All key activities were achieved ahead of the implementation schedule specified in the DRP. Table 5 provides a comparative overview of the actual progress against the tentative implementation schedule specified in the DRP.

Table 5: Actual and Tentative Implementation Schedule of Resettlement Activities

Activities	Tentative Schedule	Actual Implementation	Remarks
DRP approved by ADB	October 2025		
Contract Offer and Contract Signing with AHs	October 2025	03 October 2025	
Disbursement of Compensation to the AHs	November-December 2025	24 October 2025	
Vacation of Land by AHs (one month after compensation payment)	January 2026	N/A	
Handover of Land to MPWT by GDR	February 2026	17 November 2025	

8. GRIEVANCE REDRESS MECHANISM

22. The Grievance Redress Mechanism (GRM) established under the Subproject remains in place for the handling of any grievances in the implementation of the DRP.

23. The GRM follows the three-step process. Aggrieved AHs/APs can lodge complaints at the district, the GDR, and the Provincial levels to seek timely resolution. The authority is vested with the PGRC to make the final administrative decision if any AH/AP is not satisfied with the resolution at the District or the GDR level. If the aggrieved AH/AP is not satisfied with the decision of the District, GDR and PGRC, s/he is free to file a lawsuit at any stage in the competent court (Municipal or Provincial court, as applicable). This GRM process remains the same as provisioned in the DRP.

24. The PGRC was established on 17 March 2020 and is fully functional and operational. As of the end of the monitoring period, there have been no changes in the members of the PRGC.

25. In addition, there have been no complaints lodged by any AHs under the GRM during this monitoring period.

9. PUBLIC CONSULTATION MEETINGS

26. During the implementation of the DRP, the public consultation for pre-signing contract was held on 03 October 2015 at 8:30 am with the participation of 74AHs. The consultation prior to the provision of compensation payments, in addition, was held on 24 0ctober 2025 with the participation of 74AHs. The minutes of both meetings in Khmer and in English, attendance lists and pictures of activities are attached in the Annexes to this Report (for the purpose of confidentiality, the names of the AHs/APs and other personal information are redacted).

10. CONCLUSION AND RECOMMENDATIONS

27. The DRP has been successfully and fully implemented ahead of the planned schedule. There have been no complaints lodged by any AH. No non-compliance with the provisions in the DRP were identified and therefore no corrective actions were necessary.

List of Annexes

Annex A: Contract Signing Stage

ព្រះរាជាណាចក្រកម្ពុជា

ជាតិ សាសនា ព្រះមហាក្សត្រ

កំណត់ហេតុ

ស្តីពីការ

ប្រជុំពិភាក្សាយោបល់ជាមួយប្រជាពលរដ្ឋដែលទទួលរងនូវផលប៉ះពាល់
មុនធ្វើការចុះកិច្ចសន្យា នៅគម្រោងកែលម្អក្រាប់ក្រុងបរិស្ថានក្រុងជុំវិញបឹងទន្លេសាប
ចំណែក២ ខេត្តបន្ទាយមានជ័យ អនុគម្រោងបណ្តាញប្រព័ន្ធលូបង្ហូរទឹកកង្វក់ក្រុងសិរីសោភ័ណ

(១) ឆ្នាំពីរពាន់ម្ភៃប្រាំ ខែកញ្ញា ថ្ងៃទីសាមសិប វេលាម៉ោងប្រាំបីព្រឹក និងម៉ោងពីរសៀល , (២)ឆ្នាំពីរពាន់ម្ភៃប្រាំ ខែតុលា ថ្ងៃទីបីវេលាម៉ោងប្រាំបី និងសាមសិបនាទីព្រឹកក្រុមការងារគណៈកម្មការអន្តរក្រសួងសហការជាមួយក្រុមការងារអនុគណៈកម្មការខេត្តបន្ទាយមានជ័យ និងអាជ្ញាធរមូលដ្ឋានពាក់ព័ន្ធបានរៀបចំកិច្ចប្រជុំពិភាក្សាយោបល់ជាមួយប្រជាពលរដ្ឋ មុនធ្វើការចុះកិច្ចសន្យានៅសង្កាត់កំពង់ស្វាយ និងសង្កាត់ព្រះពន្លា ក្រុងសិរីសោភ័ណ ខេត្តបន្ទាយមានជ័យ ដែលទទួលរងផលប៉ះពាល់ដោយសារគម្រោងកែលម្អក្រាប់ក្រុងបរិស្ថានក្រុងជុំវិញបឹងទន្លេសាបជំហ៊ានទី២ ខេត្តបន្ទាយមានជ័យ អនុគម្រោងបណ្តាញប្រព័ន្ធលូបង្ហូរទឹកកង្វក់ក្រុងសិរីសោភ័ណ ដោយមានការចូលរួមពីលោក អេត រ៉ណ្ណៈ ក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់ដោយសារគម្រោងអភិវឌ្ឍន៍បានលើកឡើងថា គម្រោងកែលម្អក្រាប់ក្រុងបរិស្ថានក្រុងជុំវិញបឹងទន្លេសាបជំហ៊ានទី២ ខេត្តបន្ទាយមានជ័យ ជាហិរញ្ញប្បទានពីធនាគារអភិវឌ្ឍន៍ អាស៊ី(ADB) ហើយក្រុមការងារអន្តរក្រសួង និងក្រុមការងារអនុគណៈកម្មការខេត្ត បានចុះធ្វើការពិនិត្យអង្កេតវាស់វែងផ្ទះសម្បែងដីធ្លី និងសំណង់ផ្សេងៗ។ និងធ្វើការសម្ភាសន៍ជាមួយបងប្អូនប្រជាពលរដ្ឋដែលមានផលប៉ះពាល់នៅទីតាំងគម្រោងរួចរាល់ជាច្រើនខែមកហើយដែរ ដើម្បីជាមូលដ្ឋានសម្រាប់ការកាត់ជូនថ្នាក់ដឹកនាំក្រសួងកំពុងជាធនាគារអភិវឌ្ឍន៍អាស៊ី(ADB)ផងដែរ។

បន្ទាប់ពីបានការយល់ព្រមធនាគារអភិវឌ្ឍន៍អាស៊ី(ADB)លើផែនការសកម្មភាពដោះស្រាយផលប៉ះពាល់រួចមក គណៈកម្មការអន្តរក្រសួងនឹងរៀបចំកញ្ចប់ឯកសារដើម្បីស្នើសុំការសម្រេចពីប្រមុខរាជរដ្ឋាភិបាល ។ ក្រោយពីបានការអនុម័តលើកញ្ចប់ឯកសារពីប្រមុខរាជរដ្ឋាភិបាលរួចមក ក្រុមការងារអន្តរក្រសួង និងក្រុមការងារអនុគណៈកម្មការខេត្តបាន ចុះមកជួបប្រជុំជាមួយបងប្អូនប្រជាពលរដ្ឋដែលបានវាស់វែងរួចពីមុនមកទាំងអស់ ដើម្បីអោយដឹងពីចំនួនគ្រាក់ដែលត្រូវសងនីមួយៗ ត្រូវទទួលបាន បន្ទាប់មកក្រុមការងាររៀបចំសំណើដកសាច់ប្រាក់ដើម្បីបើកជូនប្រជាពលរដ្ឋដែលបានត្រៀមរួចស្រេច ហើយកិច្ចសន្យាជាមួយក្រុមការងារ និងទុកពេលវេលារយៈពេលពាក់ថ្ងៃដើម្បីធ្វើការរុះរើទុកទីតាំងដីអោយនៅទំនេរ ដើម្បីក្រុមហ៊ុនធ្វើការឈូសឆាយសាងសង់ផ្លូវ ។ ចំពោះការផ្តល់ប្រាក់សំណងជាគោលនយោបាយដោយផ្អែកលើការសិក្សាតម្លៃជំនួសដែលត្រូវបានសិក្សាដោយភ្នាក់ងារឯកជនដែលមានជំនាញត្រឹមត្រូវនិងច្បាស់លាស់ក្នុងការសិក្សាអចលនទ្រព្យផ្សេងៗ ។ ។

កិច្ចប្រជុំពិភាក្សាយោបល់នេះបានបញ្ចប់នៅវេលាម៉ោងដប់ព្រឹកនាថ្ងៃ ខែ ឆ្នាំ ដដែលក្រោមបរិយាកាសស្និទ្ធស្នាលនិងទទួលទុសត្រូវ ។

ឌានយ៉ីណូ និងឯកភាព	លេខាកត់ត្រា
ប្រធានអង្គប្រជុំ	
អេត ទណ្ណៈ	ឈ្មោះ កុសល្យ

Kingdom of Cambodia

Nation Religion King

Minutes of Meeting

Public consultation with the Affected Households in Contract Signing Stage Under the Second Urban Environmental Management in the Tonle Sap Basin Project Banteay Meanchey Province, the Wastewater and Drainage System Subproject in Serey Sophon City

(1) On 30 September 2025 at 8 in the morning and 2 in the afternoon, (2) On 3 October 2025 at 8:30 in the morning, the IRC-WG, together with Battambang PRSC-WG, and relevant authorities, organized public consultation meetings prior to contract signing for affected areas in Kompong Svay Commune, and Preah Ponlea Communes of Serey Sophon City, Banteay Meanchey Province. These areas are affected by the Second Urban Environmental Management in the Tonle Sap Basin Project; the Wastewater and Drainage System Subproject, located in Serey Sophon City, with the participation of Mr. Eth Vannak as the IRC-WG. He stated that the project is funded by the Asian Development Bank (ADB). The IRC-WG and the PRSC-WG have been conducting surveys and measurements of houses, land, and other structures, and conducting interviews with the AHs at the project site for several months, as a basis for reporting to ministry as well as the Asian Development Bank (ADB).

After approval of the Resettlement Plan by the ADB, the IRC will prepare and submit a budget package to seek approval from the RGC. Once the budget package is approved by the RGC, the IRC-WG, together with the PRSC-WG, will meet all AHs that have been surveyed to determine the compensation amount for each AHs. The working group will then prepare a cash withdrawal request for disbursement to households that have agreed to and signed contracts with the working group. A period of 30 days will be allocated for AHs to clear the land and leave it vacant, enabling the contractor to proceed with site clearance and construction as scheduled. The compensation rate is based on a replacement cost study conducted by an independent and qualified agency with expertise in real estate valuation.

The meeting concluded at 10 in the morning on the same dates in a friendly and responsible atmosphere.

Minute Meeting Taker

Chneang Kosal

Seen and Endorsed by

Chairman of Meeting

Eth Vannak

Attendance lists and Picture during Signing Contract Stage

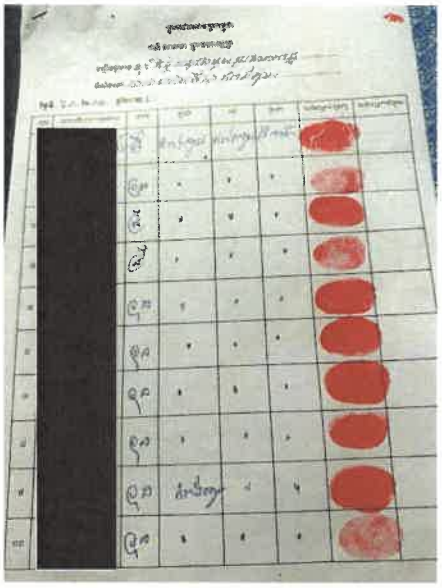

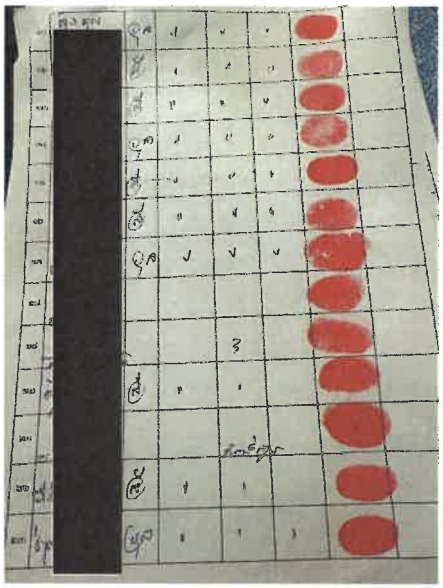

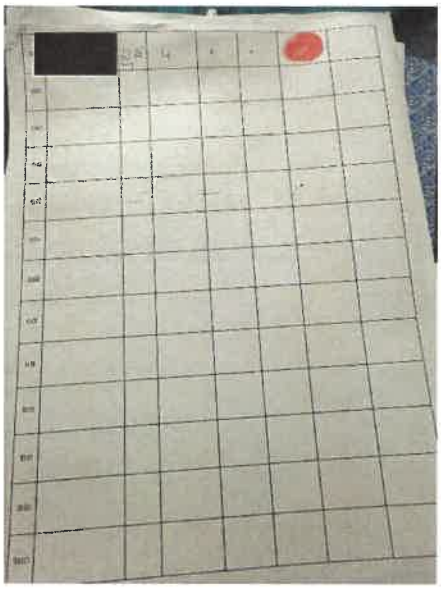

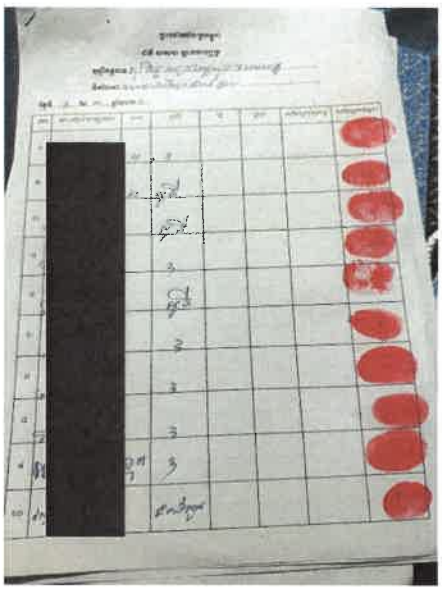

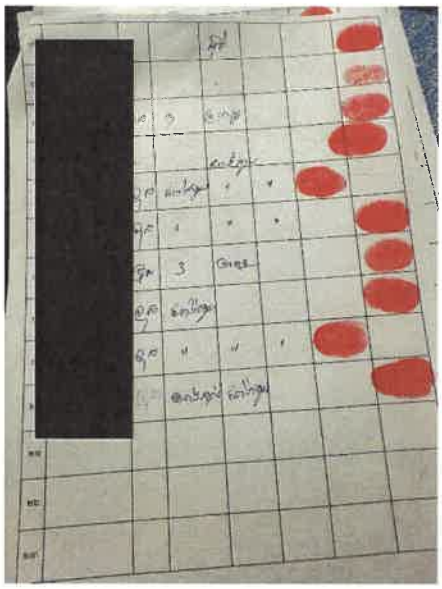

CK

Annex B: Compensation Stage

ព្រះរាជាណាចក្រកម្ពុជា

ជាតិ សាសនា ព្រះមហាក្សត្រ

កំណត់ហេតុ

ស្តីពីការ

ប្រជុំមុនពេលបើកច្រាក់ឯកត្តម្ភជាគោលនយោបាយជុនប្រជាពលរដ្ឋ ដែលទទួលរងផលប៉ះពាល់ដោយសាគម្រោងកែលម្អគ្រប់គ្រងបរិស្ថានក្រុង ជុំទី៣ចិញ្ចឹមនៃឆ្នាំ២០២០ ខេត្តបន្ទាយមានជ័យ អនុគម្រោងបណ្តាញប្រព័ន្ធលូបង្ហូរទឹកកខ្វក់ ក្រុងសិរីសោភ័ណ

(១) ឆ្នាំពីរពាន់ម្ភៃប្រាំ ខែតុលា ថ្ងៃទីម្ភៃបី វេលាម៉ោងពីរសៀល , (២)ឆ្នាំពីរពាន់ម្ភៃប្រាំ ខែតុលា ថ្ងៃទីម្ភៃបួនវេលាម៉ោងប្រាំបី និងសាមសិបនាទីព្រឹក ក្រុមការងារគណៈកម្មការអន្តរក្រសួងសហការជាមួយក្រុមការងារអនុគណៈកម្មការខេត្ត បានដឹកនាំ និង អាជ្ញាធរមូលដ្ឋានពាក់ព័ន្ធ បានរៀបចំកិច្ចប្រជុំពិគ្រោះយោបល់លើកប្រាក់ជូនប្រជាពលរដ្ឋ ចំនួនពីរសង្កាត់គឺ : សង្កាត់កំពង់ស្វាយ និង សង្កាត់ព្រះពន្លា ក្រុងសិរីសោភ័ណ ខេត្តបន្ទាយមានជ័យ ដែលទទួលរងផលប៉ះពាល់ដោយសារគម្រោងកែលម្អគ្រប់គ្រងបរិស្ថានក្រុងជុំវិញបឹងទន្លេសាបជំហាន២ ខេត្តបន្ទាយមានជ័យ អនុគម្រោងបណ្តាញប្រព័ន្ធលូបង្ហូរទឹកកខ្វក់ ក្រុងសិរីសោភ័ណ ដោយមានការចូលរួមពីលោក **អេត រ៉ាណា**: ក្រុមការងារអន្តរក្រសួង និងលោក **ង៉ែត ព្រំ** មន្ត្រីនាយកដ្ឋានត្រួតពិនិត្យផ្ទៃក្នុង នៃអគ្គនាយកដ្ឋានដោះស្រាយផលប៉ះពាល់ដោយសារគម្រោងអភិវឌ្ឍន៍ ។

ជាកិច្ចចាប់ផ្តើមលោក **អេត ទណ្ណៈ** ក្រុមការងារគណៈកម្មការអន្តរក្រសួងដោះស្រាយផលប៉ះពាល់ដោយសារគម្រោងអភិវឌ្ឍន៍បានលើកឡើងថា ក្រោយពីបង្ហូនប្រជាពលរដ្ឋដែលបានទីតាំងកំពង់រស់នៅតាមផងផ្លូវស្ថិតនៅទីតាំងគម្រោងដែលមានផលប៉ះពាល់បានព្រមព្រៀងចុះកិច្ចសន្យាជាមួយក្រុមការងាររួចនាពេលកន្លងមក ពីនៅថ្ងៃនេះក្រុមការងារបានមកប្រាក់ជូនប្រជាពលរដ្ឋដែលបានព្រមព្រៀងគ្នាលើកិច្ចសន្យាតាំងនោះ ហើយសូមបង្ហូនស្គាល់ក្រុមការងារហៅឈ្មោះនៅតាមលេខរៀងក្នុងតារាងបញ្ជីឈ្មោះរួចចូលមកកាន់តុគណៈកម្មការដើម្បីធ្វើតមដានលើបញ្ហាប្រាក់ឈ្នួលប្រាក់ជួលរបស់ក្រុមការងារ ។ លើសពីនេះទៀតសូមបង្ហូនប្រជាពលរដ្ឋពិនិត្យនិងពាក់ចិត្តអោយបានត្រឹមត្រូវជាមុនសិនទើបនៅកន្លែងផ្សេងទៀតបាន ក្នុងករណីមិនបានពាក់អោយបានត្រឹមត្រូវជាមុននឹងមានការចាត់បង់នៅកន្លែងផ្សេងក្រុមការងារមិនទទួលទុសត្រូវឡើយ ហើយបន្ទាប់ពីទទួលបានប្រាក់ទុបត្តម្ភជាគោលយោបាយនេះតទៅសូមបង្ហូនចាប់ផ្តើមធ្វើការរុះរើសំណង់ផ្សេងៗមានដើមឈើជាដើមចេញដោយក្រុមការងារទុកពេលវេលារយៈពេលជាច្រើនថ្ងៃអោយបង្ហូនធ្វើការរុះរើចេញ ដើម្បីទុកទីតាំងដីអោយនៅទំនេរជាយស្រួលដល់ក្រុមហ៊ុនធ្វើការឈ្នួលភ្ជាយសាងសង់អោយបានពេលវេលាតាមការព្រួយបារម្ភ ។

ស្ថិតក្នុងអង្គប្រជុំ ពីបងប្អូនប្រជាពលរដ្ឋមានការសប្បាយចិត្ត និងអបអរសាទរយ៉ាងខ្លាំងចំពោះគម្រោងនេះ ពីព្រោះវា បានជួយសម្រួលបន្ថែមទៀតដល់ប្រជាពលរដ្ឋក្នុងការបង្ហូរទឹកកខ្វក់ចេញពីលំនៅដ្ឋាន

កិច្ចប្រជុំពិគ្រោះយោបល់នេះ បានបញ្ចប់នៅវេលាម៉ោងដប់ព្រឹកនាថ្ងៃ ខែ ឆ្នាំ ដដែលក្នុងបរិយាកាសស្ថិតស្ងាត់ និងទទួលទុសត្រូវខ្ពស់ ។

ដានយើញ និងឯកភាព	លេខាកត់ត្រា
ប្រធានអង្គប្រជុំ	
	ឈ្មោង កុសល្យ
អេត ទណ្ណៈ	

Kingdom of Cambodia

Nation Religion King

Minutes of Meeting

Public consultation in Compensation Stage for the Affected Households Under the Second Urban Environmental Management in the Tonle Sap Basin Project Banteay Meanchey Province, the Wastewater and Drainage System Subproject in Serey Sophon City

(1) On 23 October 2025 at 2 in the afternoon, (2) On 24 October 2025 at 8:30 in the morning, the IRC-WG, together with the Battambang PRSC-WG, and relevant authorities, organized public consultation meetings for the compensation payment to the AHs in two communes: Kompong Svay Commune, and Preah Ponlea Commune, Serey Sophon City, Banteay Meanchey Province. These areas are affected by the Second Urban Environmental Management in the Tonle Sap Basin Project located in Banteay Meanchey province, the Wastewater and Drainage System Sub-Project in Serey Sophon City, with the participation from **Mr. Eth Vannak**, the IRC-WG and **Mr. Nget Prom** from DIMDM of the GDR.

First, **Mr. Eth Vannak**, the IRC-WG, stated that the AHs who had previously agreed and signed compensation contracts with the working group were invited to receive their compensation payments. Participants were requested to listen carefully as their names would be called according to the official list to sign and receive the payment. He further advised residents to carefully check and count the compensation amount before leaving the payment area, noting that the working group would not be responsible for any discrepancies identified afterward. Following receipt of compensation, the AHs were informed of the policy requirement to dismantle affected structures and remove trees. A period of 30 days was granted for dismantling and clearing the land to ensure its vacant and ready for construction activities according to the project schedule.

During the meeting, residents expressed satisfaction and appreciation for the project, noting that it would improve drainage and waste management conditions for their households and community.

The public consultation concluded at 10 in the morning on the same dates in a friendly and responsible atmosphere.

Minute Meeting Taker

Chneang Kosal

Seen and Endorsed by

Chairman of Meeting

Eth Vannak
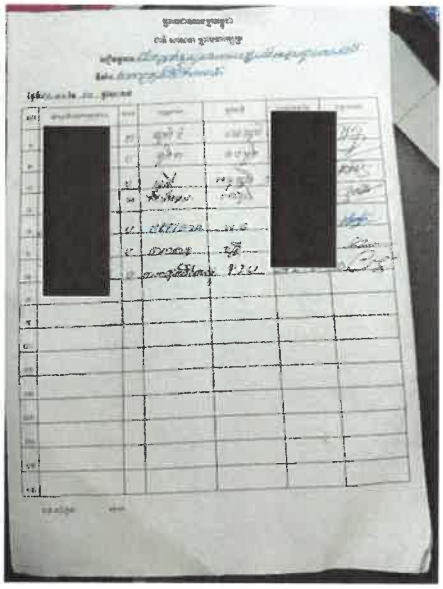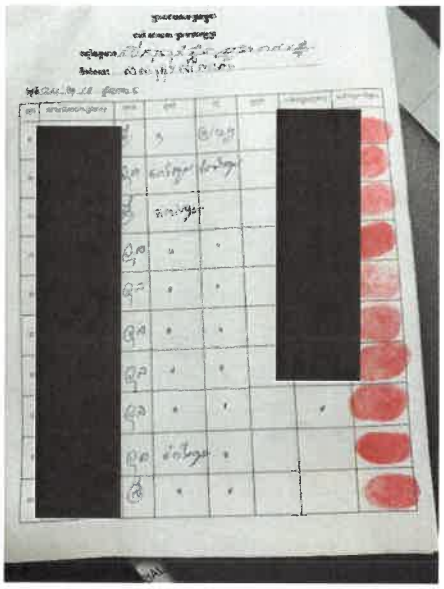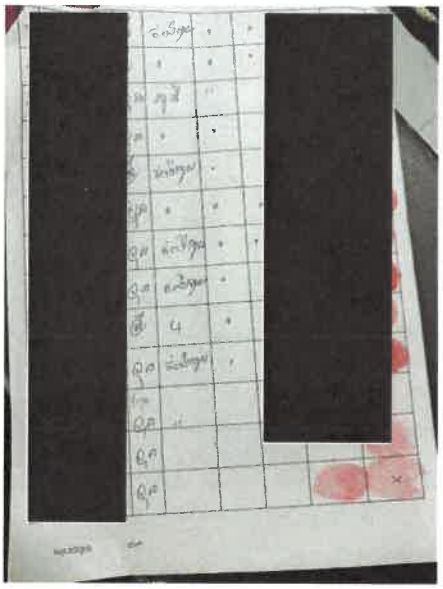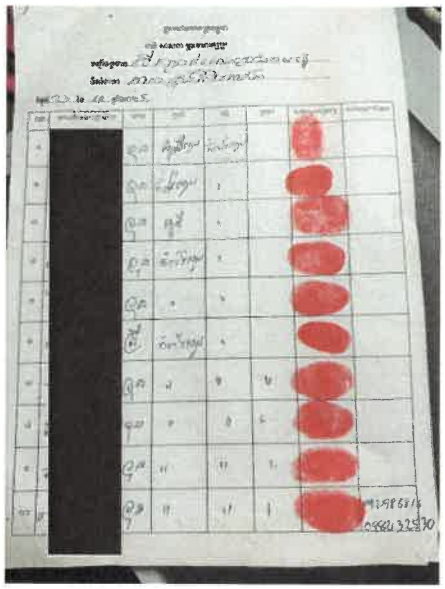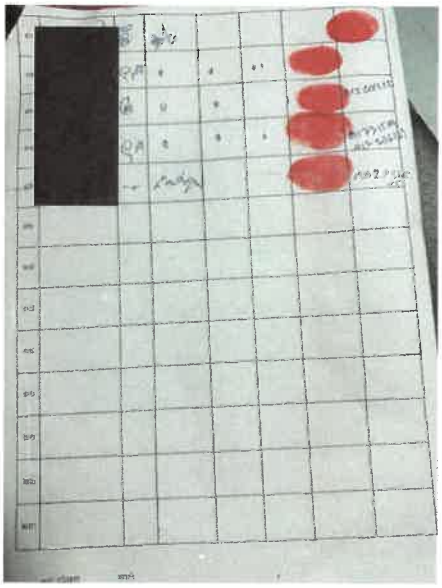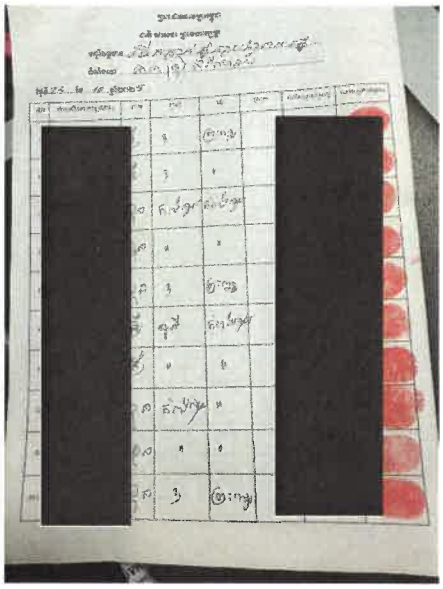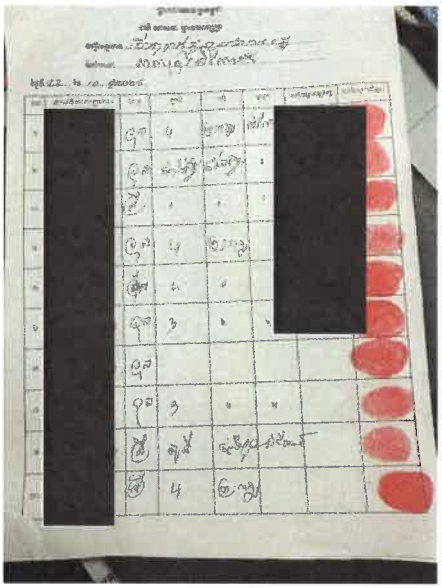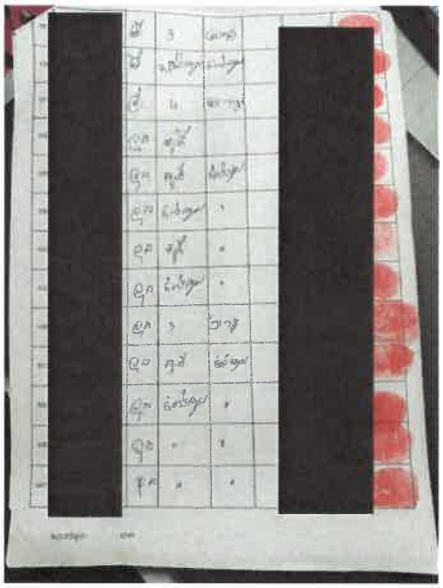
Attendance Lists and Photos during Compensation Stage
